

POLIO | GLOBAL ERADICATION INITIATIVE

Overview of country planning: Progress and Challenges

BILL & MELINDA
GATES foundation



Mike McGovern
Chair, Transition Management Group
Meeting of the Polio Partners Group
Geneva, 8 December 2017



Outline

- Overview of progress in the development of country plans
- Challenges and how TMG is planning to address them

Progress at a glance: Then... (end of 2016)

Country	Communication initiated	Governing body established	Mapping of assets	Mapping of priorities	Transition strategies agreed	Transition plan drafted and costed	Transition plan finalized and funding agreed
Afghanistan	<i>Afghanistan is an endemic country. Planning expected after interruption of transmission.</i>						
Angola	Complete	Complete	Complete	In process	Not yet started	Not yet started	Not yet started
Bangladesh	Complete	N/A	In process	In process	Not yet started	Not yet started	Not yet started
Cameroon	Complete	Complete	Complete	Complete	Not yet started	Not yet started	Not yet started
Chad	Complete	In process	Complete	In process	Not yet started	Not yet started	Not yet started
DR Congo	Complete	In process	Complete	In process	Not yet started	Not yet started	Not yet started
Ethiopia	Complete	Complete	Complete	In process	Not yet started	Not yet started	Not yet started
India	Complete	Complete	Complete	Complete	Complete	Complete	In process
Indonesia	Complete	N/A	In process	In process	Not yet started	Not yet started	Not yet started
Myanmar	Complete	Not yet started	Not yet started	Not yet started	Not yet started	Not yet started	Not yet started
Nepal	Complete	Complete	In process	In process	Not yet started	Not yet started	Not yet started
Nigeria	Complete	Complete	Complete	In process	In process	Not yet started	Not yet started
Pakistan	<i>Pakistan is an endemic country. Planning expected after interruption of transmission.</i>						
Somalia	Complete	Not yet started	Not yet started	Not yet started	Not yet started	Not yet started	Not yet started
South Sudan	Complete	Unknown	Complete	In process	Not yet started	Not yet started	Not yet started
Sudan	Complete	Complete	In process	In process	Not yet started	Not yet started	Not yet started

Country Planning Dashboard as of Dec 8, 2016

Updated monthly on the GPEI website, here: http://polioeradication.org/wp-content/uploads/2017/10/country-planning-dashboard_03October2017.pdf



Progress at a glance: Now...(end of 2017)

Country	Communication initiated	Coordination body established	Mapping of assets	Mapping of priorities	Transition strategy agreed	Transition plan drafted and costed	Transition plan finalized and funding agreed
Afghanistan	<i>Afghanistan is an endemic country. Planning expected after interruption of transmission.</i>						
Angola	Complete	Complete	Complete	Complete	In process	In process	Not yet started
Bangladesh	Complete	N/A	Complete	Complete	Complete	In process	In process
Cameroon	Complete	Complete	Complete	Complete	Complete	Complete	In process
Chad	Complete	Complete	Complete	Complete	Complete	Complete	Not yet started
DR Congo	Complete	Complete	Complete	Complete	Complete	Complete	In process
Ethiopia	Complete	Complete	Complete	Complete	In process	In process	Not yet started
India	Complete	Complete	Complete	Complete	Complete	Complete	In process
Indonesia	Complete	N/A	Complete	Complete	Complete	Complete	Not yet started
Myanmar	Complete	N/A	Complete	Complete	Complete	Complete	In process
Nepal	Complete	Complete	Complete	Complete	Complete	Complete	In process
Nigeria	Complete	Complete	Complete	Complete	In process	Not yet started	Not yet started
Pakistan	<i>Pakistan is an endemic country. Planning expected after interruption of transmission.</i>						
Somalia	Complete	Not yet started	Complete	In process	Not yet started	Not yet started	Not yet started
South Sudan	Complete	Complete	Complete	Complete	In process	In process	Not yet started
Sudan	Complete	Complete	Complete	Complete	Not yet started	Not yet started	Not yet started

Country Planning Dashboard as of December 1, 2017

Updated monthly on the GPEI website, here: http://polioeradication.org/wp-content/uploads/2017/10/country-planning-dashboard_03October2017.pdf



Are we measuring what matters?

Quality of the process

- Is the plan fully owned by the Government?
- Are all stakeholders fully engaged in the planning process, providing input (MoH, MoF, development partners) ?

Quality of the plans

- Is the plan **aligned with national health priorities** and processes?
- Does the plan have a **realistic and sustainable financing strategy**, including domestic resources, and with a detailed budget for specific activities?
- Does the plan entail elements for **national capacity building**, with a gradual transfer of responsibilities to the Government?
- Is there a plan for ensuring **sustainable implementation of the polio essential functions**, mainstreaming into existing structures (e.g., broader disease surveillance and outbreak response mechanisms)?

Draft country plans at a glance

- **8** countries have draft transition plans
- **4** include details on how polio essential functions will be mainstreamed
- **3** include a detailed budget
- **5** have a financing strategy
- **7** include provisions for domestic funding

*Most of these are **early drafts**, to be discussed further at country level.*

*We expect them to go through significant refinement
in the next six months.*



Challenge 1: Timing

- The planning process is taking longer time than initially foreseen. Not all countries will have draft plans by end 2017
- Dilemma between “moving fast” and “ensuring quality”

PROPOSED WAY FORWARD:

- Re-inforce messaging on the ramp down – “GPEI budget reductions are a reality”
- Targeted advocacy and support to those countries lagging behind

Challenge 2: Country Ownership

- The process is still being led at the “technical level” . There is a not sufficient high level ownership of the process

PROPOSED WAY FORWARD:

- Develop a detailed **high level advocacy strategy** to better engage Ministers (Health/Finance/Budget & Planning) and WHO/UNICEF Country Representatives
- Build **WHO and UNICEF Regional Office and Country Office capacity** to lead, with the goal of having them drive the process by June 2018 .


Challenge 3: Quality

- Many of the plans assume WHO/UNICEF support will continue over the long term, at the same levels
- Polio essential functions still need to be fully embedded into the draft plans
- **PROPOSED WAY FORWARD:**
 - Communicate **quality indicators**, emphasizing the importance of national capacity building and sustainability
 - Share **best practices** (e.g. Nepal's plans to build government ownership over time)
 - Share **PCS guidance** with countries, detailing roles and responsibilities of countries to sustain a polio-free world

Challenge 4: Sustainability

- Few draft plans have identified sustainable financing options. There is an expectation for external funding support to continue
- Few plans include domestic funding options and are requesting resource mobilization support/guidance
- Likely for plans to remain on the shelf in fragile and conflict affected states, with limited funding options
- **PROPOSED WAY FORWARD:**
 - **Engage the TIMB to help expand the scope of discussions,** especially for joint approaches to supporting fragile, conflict affected countries
 - **Advocate for domestic funding options** (e.g. Africa Immunization Business Case)
 - **Communicate upcoming in-country stakeholder meetings** (e.g., Cameroon in early December)

Targeting June 2018 for final plans, while building regional and country office ownership

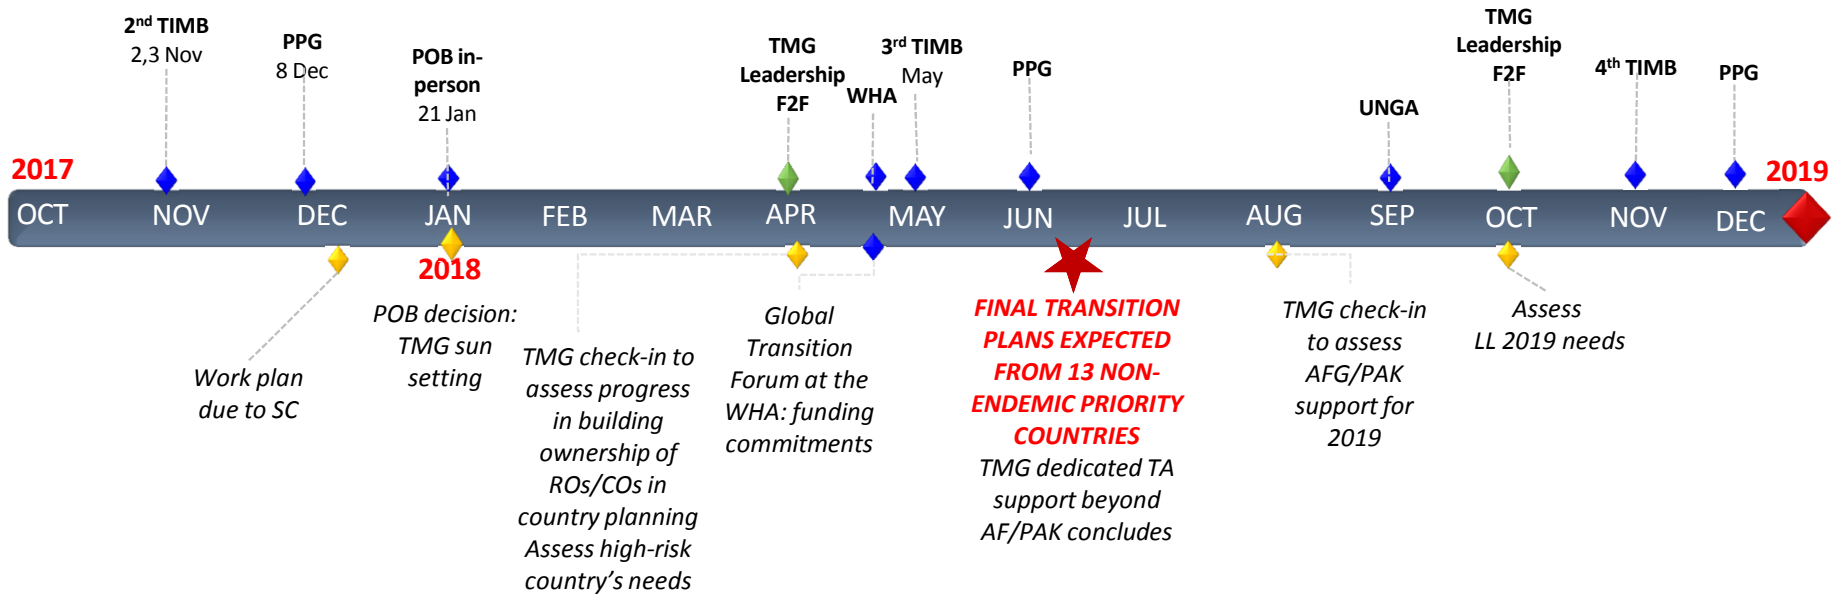

TMG to strengthen RO/CO role in country planning support

Streamlined support for AFG and PAK based on best practices from other countries

Lessons Learned activities continue



THANK YOU
